



11-17-2003

Peirce Island Pool Discharge Elimination

Natalie Landry

New Hampshire Department of Environmental Services

Follow this and additional works at: <https://scholars.unh.edu/prep>



Part of the [Marine Biology Commons](#)

Recommended Citation

Landry, Natalie, "Peirce Island Pool Discharge Elimination" (2003). *PREP Reports & Publications*. 325.
<https://scholars.unh.edu/prep/325>

This Report is brought to you for free and open access by the Institute for the Study of Earth, Oceans, and Space (EOS) at University of New Hampshire Scholars' Repository. It has been accepted for inclusion in PREP Reports & Publications by an authorized administrator of University of New Hampshire Scholars' Repository. For more information, please contact Scholarly.Communication@unh.edu.

Peirce Island Pool Discharge Elimination

A Final Report to

The New Hampshire Estuaries Project

Submitted by

Natalie Landry

New Hampshire Department of Environmental Services

360 Corporate Drive

Portsmouth, NH, 03801



November 17, 2003

This report was funded in part by a grant from the Office of State Planning, New Hampshire Estuaries Project, as authorized by the U.S. Environmental Protection Agency pursuant to Section 320 of the Clean Water Act.



Table of Contents

Executive Summary	1
List of Tables	1
List of Figures	1
Introduction	1
Project Goal.....	1
Methods	2
Results and Discussion	2
Conclusions.....	3
Recommendation.....	3

Executive Summary

The City of Portsmouth maintains a public swimming pool on Peirce Island which is situated in the Piscataqua River and accessed by a bridge in downtown Portsmouth. The swimming pool filter backwash discharged to the Piscataqua River. In 2002, the City applied for a New Hampshire Estuary Project grant with the goal of eliminating the direct discharge. The grant was awarded to the City through the New Hampshire Department of Environmental Services. Using the grant funds and local cash and in kind services, the City installed a pump system and new piping to deliver the filter backwash to the Peirce Island wastewater treatment facility via a force main.

List of Tables

Table 1 Proposed Project Budget.....	3
--------------------------------------	---

List of Figures

Figure 1 Schematic of Peirce Island Pool.....	2
---	---

Introduction

The Peirce Island Pool is owned by the City of Portsmouth and serves approximately 19,000 swimmers each summer. The pool was originally constructed in the 1930s and updated in the 1970s and again in the mid 1990s. The pool's 800,000 gallons of water were cleaned through a rapid sand filter. The filter was then cleaned through a backwash process and that wastewater was discharged directly into the Piscataqua River which is part of the Great Bay Estuary. The City sought and was awarded funds through the New Hampshire Estuaries Project (NHEP) to eliminate the direct discharge to the River. The NHEP Workplan reference number for this project is 03-A-3.

Project Goal

The goal of the Peirce Island Pool Discharge Elimination project was to remove the direct discharge of pool filter backwash that flows into the Piscataqua River.

Methods

The City of Portsmouth applied for a NHEP grant in 2002. The NHEP transferred funds to the New Hampshire Department of Environmental Services (DES) through a memorandum of agreement that authorized DES to enter into a grant agreement with the City and manage the project. The New Hampshire Governor and Executive Council granted approval of a grant agreement between the DES and the City on February 19, 2003, Item #62 for \$15,000.

The City installed a pump facility to provide the appropriate lift so the discharge could be connected with the 24" force main. Pipe lines were also installed to connect the pool filter to the pump chamber. The 8" discharge pipe leading into the Piscataqua River was cut and capped. Figure 1 illustrates the proposed design. All construction was completed in accordance with the plans and the filter backwash was redirected to the wastewater treatment plant.

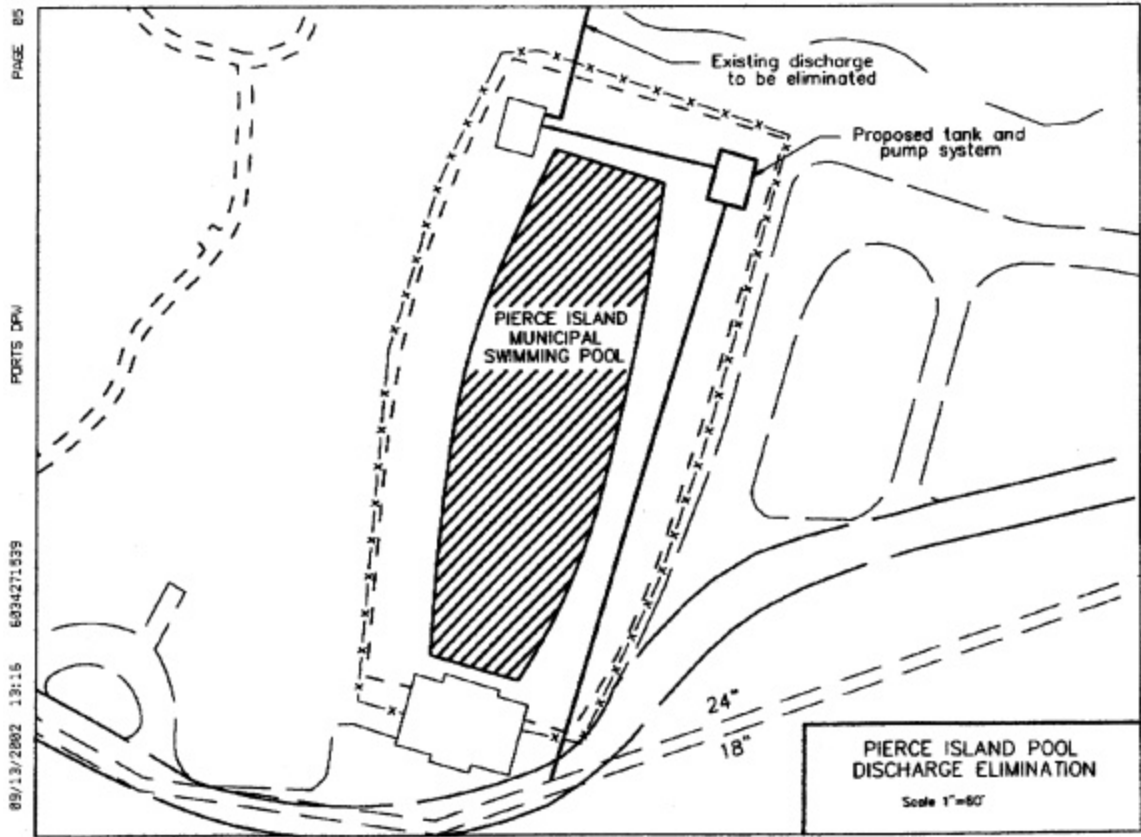


Figure 1 Schematic of Peirce Island Pool

Results and Discussion

All construction took place during June 2003. The project was successfully completed. The discharge to the River was capped and the filter backwash is now routed through the new pipeline and pump system to the force main which connects to the Peirce Island wastewater treatment plant. The

City of Portsmouth provided local matching funds and in kind services which totaled \$179,560. This exceeded the minimum required local match of \$55,546.00 (see Table 1). By eliminating the pool filter backwash, a source of bacteria and chemicals that flowed into the Piscataqua River has been removed. The elimination of this discharge works toward the overall goal of improving water quality in the Great Bay Estuary watershed.

Table 1 Proposed Project Budget

Item	Quantity/Rate	Grant	Match	Total
Equipment	Dump Truck 1 ea @ \$40/day	200	200	400
Equipment	Backhoe 1 ea @ \$40/day	200	200	400
Equipment	Pick-up 1 ea @ \$10/day	50	50	100
Labor	3 man crew @ \$360.40	1,802	1,802	3604
Materials	Gravel	200	200	400
Materials	8" DI – 550 lf	2,350	2,350	4,700
Materials	24X8 tap sleeve	600	600	1,200
Materials	2-8" elbow 45 MJ	74	74	148
Materials	2-8" check valve	1,050	1,050	2,100
Materials	8" tap gate MJ	233	233	466
Materials	Gate box	14	14	28
Materials	5000 gal vault	2,500	2,500	5,000
Materials	25hp duplex system	5,727	21,273	27,000
Contract service	Electrical		10,000	10,000
Contract service	Pump Install		15,000	15,000
Totals		\$15,000	\$55,546	\$70,546

Conclusions

The City of Portsmouth has met all the requirements of the Grant Agreement and submitted match documentation and an invoice to DES. The elimination of this contamination to the Piscataqua River has been successfully completed.

Recommendation

The NHEP should consider funding similar projects that result in the removal of illicit discharges to tidal waters. Infrastructure improvement projects are typically expensive and the financial partnering by NHEP assists communities in meeting the growing needs of replacing aging infrastructure.
