

More Kids, Brighter Futures

Expanding the Union Street Clubhouse to Meet the Needs of the Community

Michael J. St. Onge

M.S. in Project Management

2021


Granite State College

More Kids, Brighter Futures

Three phase capital campaign to increase the Club's capacity from 4,000 kids per year to 6,000 kids per year:

- Phase 1: raise \$5.2 million
- Phase 2: renovate Club's summer camp, Camp Foster
- Phase 3: Add 4800 square feet addition to the Club's Union Street building.

Manchester, NH

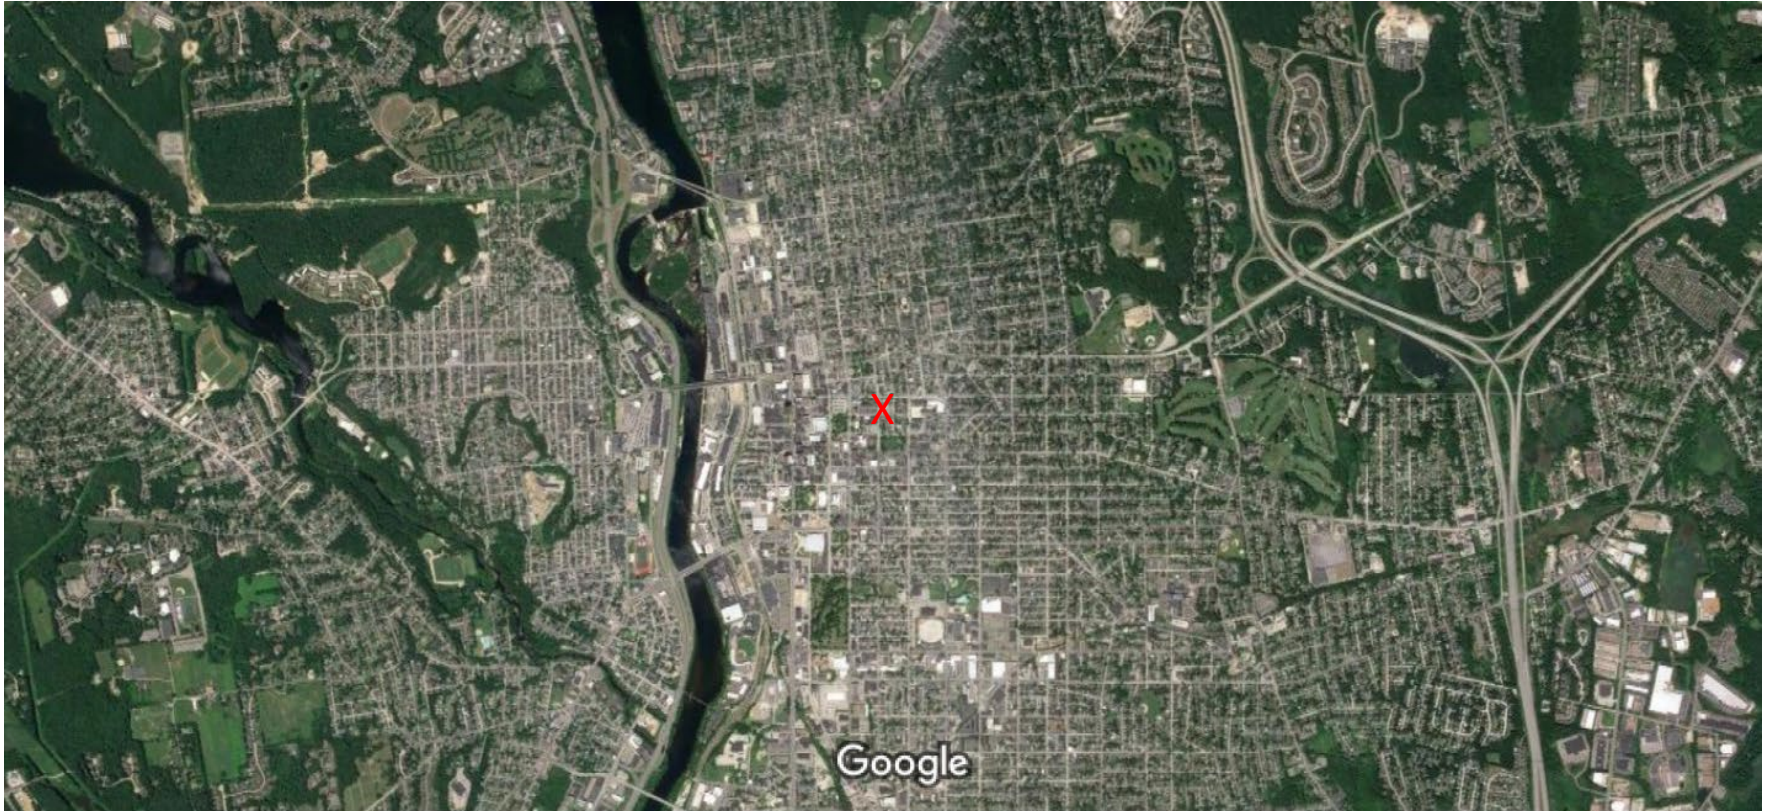

Granite State College

View of Club before construction



Granite State College

Architect conceptual drawing



Granite State College

Budget

- Capital campaign goal: \$5.2 million
- Camp Foster upgrade cost estimate: \$2.8 million
- Union Street Addition cost estimate: \$2.1 million (costs were lower than expected)
- Cash available at time of Union Street construction: \$1.3 million
- Endowment funds used: \$1 million
- Remaining balance after all costs paid and all pledges received: \$368,961



Construction



Granite State College

Completed Project



Granite State College

Risk and Opportunities

- Funding shortage – identified on risk register
- COVID-19 Global Pandemic – added to risk register
- Surprise donation – notice given very late in project

Lessons Learned

- Involve key stakeholders early in project
- Risk identification – you won't foresee everything, prepare to be flexible
- Surprise events can be positive or negative
- As a non-profit, don't be afraid to ask contractors and vendors for donations
